



Ethiopian National Theatre Building Project (2B+G+11)

Construction Project Monthly Report of July 2022

Client


Federal Government Building Construction project Office

Consultant

Addis Mebratu Consultant Architects and Engineers

Contractor

OVID Construction Plc

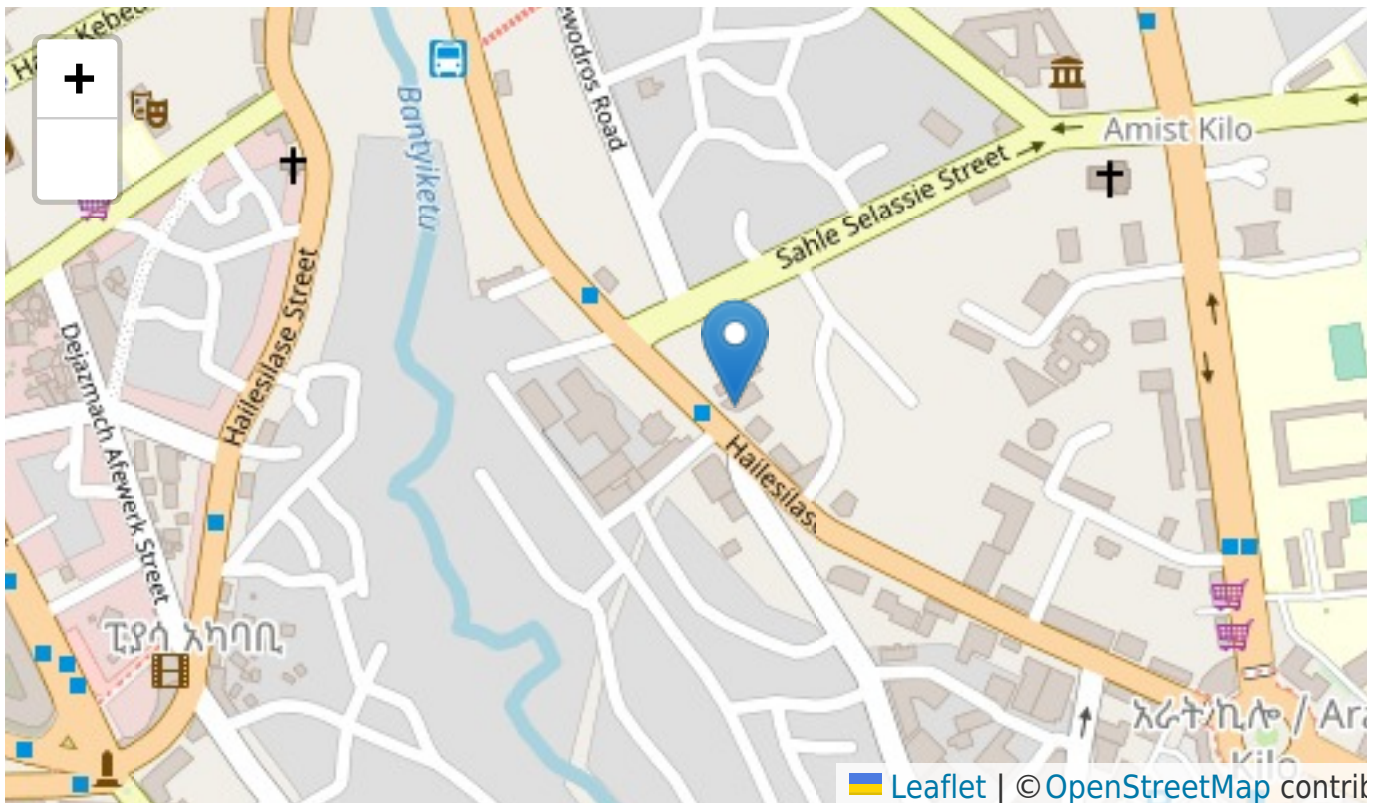

null, null, null, null, null

Time Information

No	Contract time	Description
1	Date of signing contract	Jan 10 22
2	Date of site handover	Feb 10 22
3	Mobilization period	Invalid date
4	Commencement date	Mar 23 22
5	Project duration	
6	Original completion date	Jan 16 25
7	Total approved extension of time	0

Finance Information

No	Contract price		
	Description	Amount in birr	Percent (%)
I	Main contract price	2,727,666,141	
II	Rebate		
III	Variation		
IV	Omission		
V	Supplement		
VI	Special condition		
VII	Total contract price	2,727,666,141	

Payment Information

No	Project payment		
	Description	Amount in birr	Percent (%)
I	Interim payment (paid for work done)		
II	Retention		
III	Remaining amount	2,727,666,141	
IV	Advance payment		
V	Repaid advance payment	12,345	
VI	Outstanding advance payment	12,345	

Bond

No	Bond Description	Amount in birr	status
I	Performance bond status/ amount		0 days remaining
II	Advance bond status/ amount		0 days remaining

Monthly Performance

6/2022	Actual	Planned
Manpower	1866767.28	1920890.4300000002
	▼	97.182392646
Direct Labour	1095096	1131593.77
Indirect Labour	771671.28	789296.66
Material	15740712.41	28220180.55
Machinery	1633855.75	3043960
Sub Contractor	6620497.81	7035039.92
Other Expense	2512892	1606447.79
Subtotal	▲	
Overhead		20
project Expense	28374725.25	
Financial	16659219.93	33083422.56
Profit		-17108399.87
Physical	(%)	

Quality Control Test

Tilte	Description
-------	-------------

Challenges

Not Found

Risks

Not Found

Instructions

Not Found

Claims

Tilte	Description
-------	-------------

Site Pictures

Evaluations

Project Evaluation

Name	This Year	This quarter	Last month	Jul
 Quality			0	0
Contractor understood and complied with constrction standards, safety & environmental requirements			0	0
Contractor used speciflicated material; quality of test and workmahship (contractors work) met contract documents or obligations			0	0
Contractor promomtly corrected defective work (remedial work) as project progressed			0	0
Contractor has performed with technical excellence, provided progress reports and required documentation			0	0
 Health And Safety			0	0
Contractor met the environmental requirements of the contract			0	0
Contractor met the required PPE and necessary safety equipment			0	0
Contractor had put together safety plan, provided safety personnel and conducted safety toolbox on regular basis			0	0
Contractor reported all injuries and damages associated with the project			0	0

Consultant Evaluation

Name	This Year	This quarter	Last month	Jul
 Quality			0	0
Contractor understood and complied with constrction standards, safety & environmental requirements			0	0
Contractor used speciflicated material; quality of test and workmahship (contractors work) met contract documents or obligations			0	0

Contractor promptly corrected defective work (remedial work) as project progressed	0	0
Contractor has performed with technical excellence, provided progress reports and required documentation	0	0
Health And Safety	0	0
Contractor met the environmental requirements of the contract	0	0
Contractor met the required PPE and necessary safety equipment	0	0
Contractor had put together safety plan, provided safety personnel and conducted safety toolbox on regular basis	0	0
Contractor reported all injuries and damages associated with the project	0	0

Contractor Evaluation

Name	This Year	This quarter	Last month	Jul
Quality			0	0
Consultant's design met building code and standards and satisfies the scope of the services			0	0
Consultants' Construction documents (drawings, specifications and addenda) were complete and accurate with minimal design errors, omissions or addenda			0	0
Consultant actively participated in meetings and addressed client's need and objective			0	0
Consultants' professionalism & ethics was well practiced			0	0
Health And Safety			0	0
Consultant enforced that the health, safety & environmental regulations (e.g. PPE and safety equipment, etc.) are met			0	0
Consultant reviewed daily work reports, documents, and studies			0	0

Consultant adequately reviewed tests and works made according to standard/specification	0	0
Consultant adequately reviewed and approved shop drawings and construction works to ensure HSE	0	0

Appendix

Inter office memo

No	Description
----	-------------

Minutes of meeting

No	Meeting Date	Subject	Description
----	--------------	---------	-------------

Site book notes

No	Description
----	-------------
